Kitchell/BRj/Seville

Sign in Sheet

701 South Mount Vernon, San Bernardino CA 92410

PH: (909) 909-693-3160 FX: (909) 889-9952

PROJECT:

SBVC Auditorium Renovation Project

Meeting:

Design Development Review (M&O Department)

Date:

03/29/2012

Time:

10:00 a.m. – 12:00 p.m.

Place:

KBS Site Office

NAME	COMPANY	SIGNATURE	EMAIL
Guilleamo Parre	SBYC	Julha	gparra Q VALLEYCOLEGE, EDV.
JIM King	SBVC	Jun Hing	
Brook	KB5	Por	
SOLBAIRD	P25	JuBil	SOWNWEBADO@PZSEVE.COM
Yao-chien Lee	NTO	youll be	ylee@ntd.com
Laura McLucas	NTD	Chen	Curcluces utd Con
JASON SMITH	KNA (Jam SD	ismithe knaconsulting.com
LEIBHANNE JONES	Mp .	B	ljones enta.com
Codenceroller	KPS	6 au	commiline Kitchellicom
Vim HANGEN	SBVC (Ha-	jhansen@stocd.cc.ca.us
RON REYES	FBS	M	ron. reyes @ Lrjassociatas. com

Kitchell/BRi/Seville

701 S. Mount Vernon, San Bernardino, CA 92410

Phone (909) 693-3160 - FAX (909) 889-9952

DATE:

March 29, 2012

MEETING:

SBVC Auditorium DD Review with M&O

TIME:

10:00 AM - 12:00 PM

LOCATION:

KBS Site Office

- ARCHITECTURAL SUMMARY NTD ARCHITECTS
- II) MEP SUMMARY P2S Engineers
- III) DESIGN SUMMARY NTD CONSULTANTS
- IV) REVIEW OF DISTRICT STANDARDS POWER CONDITIONING & IT power (RO AMEN)
 - a. NTD to verify District Standards incorporated to date
 - b. Identify outstanding items for proposal or no cost substitution
 - c. Elevator discussion KONE
- V) FEEDBACK M&O Department

VI) Q & A

1) NTD (LAJ) - DISCUSSED TEMP CHILLER DEMO SCHEDULE (W/CP)

- SITE ARRAY
- NEW ELEVATOR
- SUMMARY OF ATRCH SPACES
- ELEVI NO MACHINE 1200M, HOKE WITH HIP AS ADTALT - Annen RUST ROOM (, LIFT KOHE- PLUKI- PROPRIETARY STATISTING - OK WSBUL
 - NO SPAINING @ STACE SPANE
 - STAIR TOWER NOT TO BE USED
 - WINDOWS REPAIRED WE REPLACED (MAKE IN-OPERAGUE)
 - noons (18x7) REFUNGISHES (HARDWARE), NEW INT DOORS - EXT PAINTEN, THE REPAIRED
 - JIM- EXT METAL ITEMS C CATINANIC INFORM NTD WHAT CAN BE RAMOVED

-BOILER ROOM	MC - TIVIN TO GLORM BRADIN
STRUCTUREN - JASON - OVERVIOU OF SLAB	euts d'appoint.
- NOW ELEV. TOWN SPPERATE	France Black
- STAIN AREA 2-WINE	•
UND - SIMEWANG - AMA	
-NEW GAT MEHTINZ	
- NEW AN SYSTEM	
- NAME PLATE DEDICATION ON SPATS ROMOVERS & RE-INSTAURN BY	curthauton
925 - 5/Ac	
- EXPLAINAD MAS	1 CP/- CHILLER REMOVAL
- FULLY OCCUPIED SPANE - 100% EXOT AIR	- romo Ator?
- HOT WOTER POILOR	
- NOW FAN COILY	
- Among Motheral East a 23000	
It - Conversion w/ ACOUSTIC way	
Darmen - son	
-TRANSFORMEN PROMATHINE	
- the poin paracates	
- CHECK LIGHT/MOTION SONSONS	
Momo - LICICOUNT FRATURE	A STATE OF S
- WChron C suragin	
PUMBING - CAL	

-From STNEY

- SUPT WASON


- WATER HEATTER


SAN BERNARDINO VALLEY COLLEGE


AUDITORIUM FF + E


Product Recommendation REVISION ONE 2010-0336-03

February 25, 2013

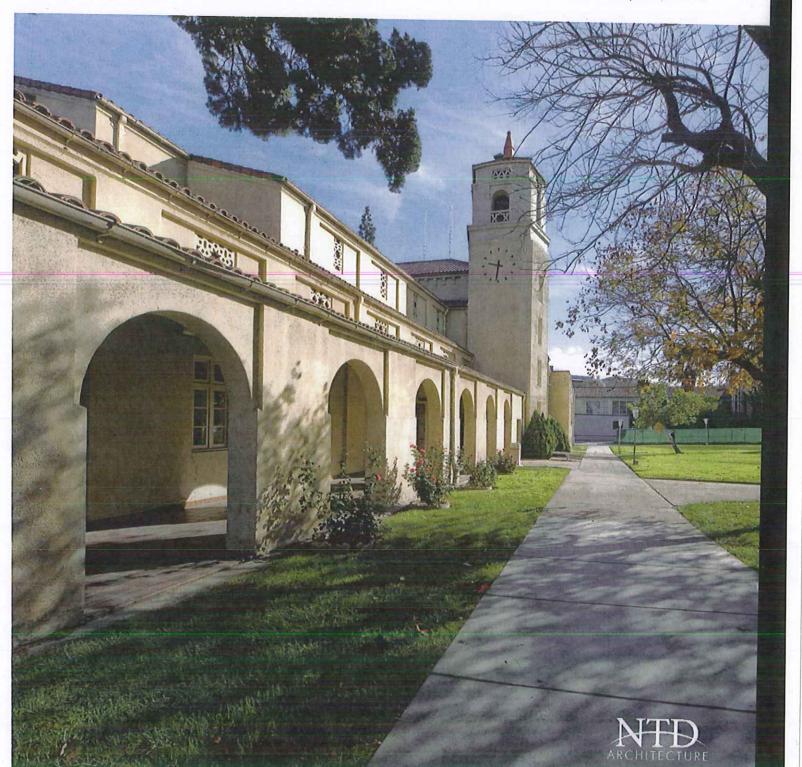




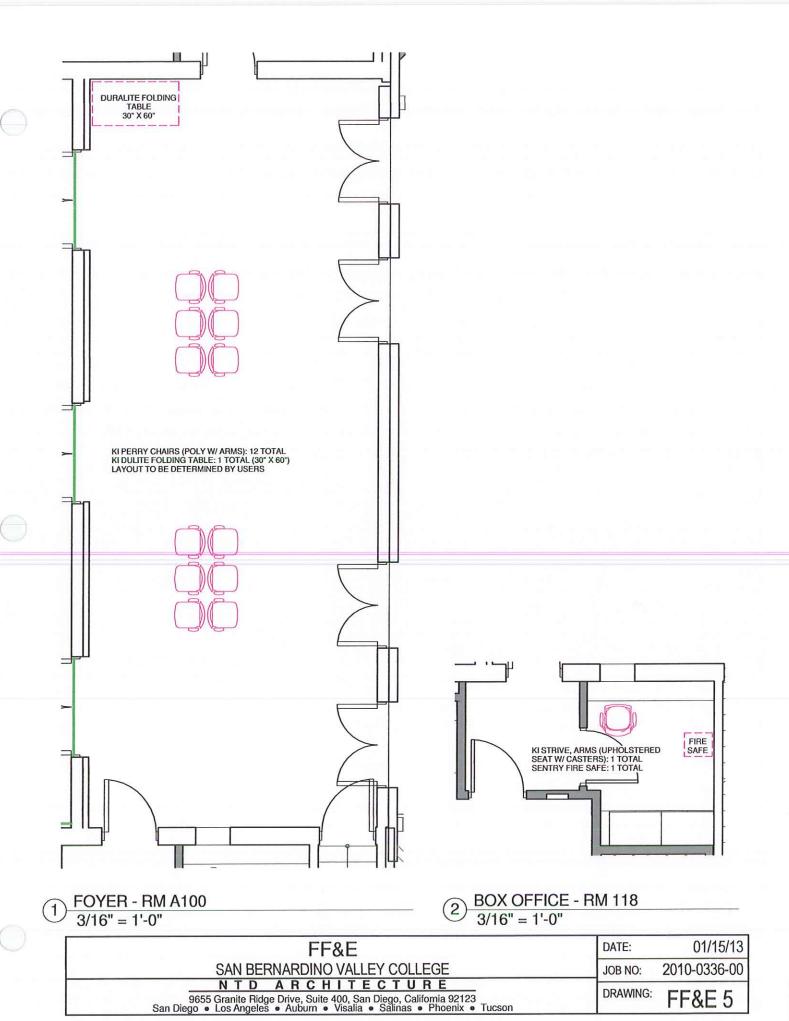


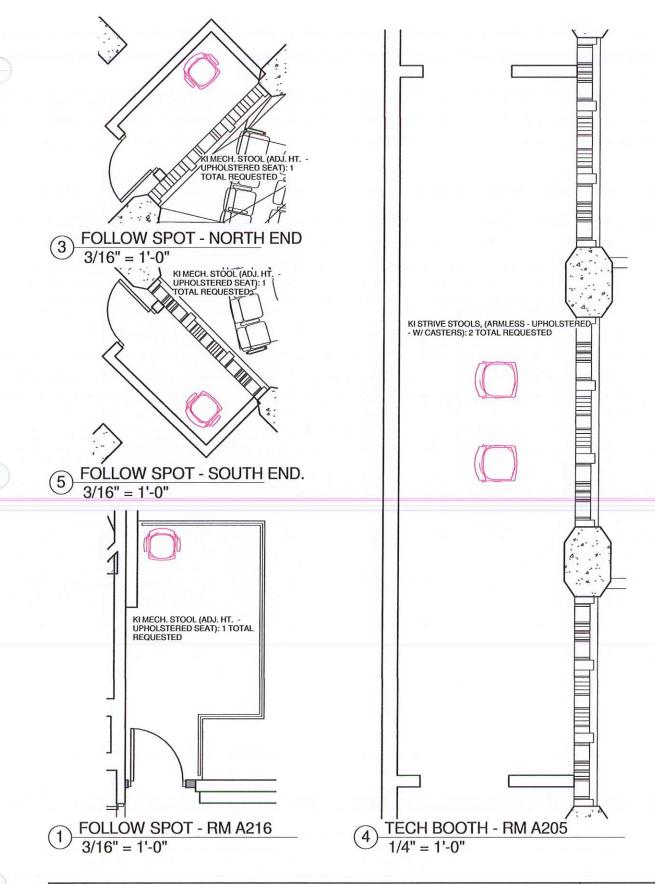

FF&E	DATE:	01/16/13
SAN BERNARDINO VALLEY COLLEGE	JOB NO:	2010-0336-00
NTD ARCHITECTURE	DRAWING:	FEOFO
9655 Granite Ridge Drive, Suite 400, San Diego, California 92123 San Diego • Los Angeles • Auburn • Visalia • Salinas • Phoenix • Tucson	DIVAVVING.	FF&E 6



DRESSING ROOM - A112 3/16" = 1'-0"



2 DRESSING ROOM - A212 3/16" = 1'-0"

FF&E	DATE:	01/21/13
SAN BERNARDINO VALLEY COLLEGE	JOB NO:	2010-0336-00
NTD ARCHITECTURE 9655 Granite Ridge Drive, Suite 400, San Diego, California 92123 San Diego Los Angeles Auburn Visalia Salinas Phoenix Tucson	DRAWING:	FF&E 7

Approved by user group 1/25/13

Strive® Task Seating



Bringing the benefits of flex seating to more people.

- Simplicity
- Comfort
- Affordability



Furnishing Knowledge*

Simple, yet elegant chair design.



Versatile.

Strive's simple, yet elegant style is an able task chair solution for corporate interiors, education and healthcare markets. Available with poly or upholstered seats. In addition to task chairs and task stools, Strive offers a consistent design language in an extended seating line that includes 4-leg, sled-base and caster-base stack chairs, high-density stack chairs, café stools, nesting chairs, task chairs, tandem eating, and fixed seating.

Strive[®] Task Chair

Designed by Giancarlo Piretti, Strive offers low-cost flex comfort in a versatile task chair.

Simplicity

Strive's clean, elegant form embodies simplicity. It flexes with back slats (nothing mechanical). The simple design blends with a wide variety of architectural styles. And, it's 100% recyclable.

Comfort

Strive's flex back encourages movement, relaxation and enhanced circulation. The radiused back conforms to the user's back for exceptional support. The contoured seat dissipates pressure points for greater comfort.

Affordability

Using readily available, recyclable materials, a small number of components and minimal assembly, Strive results in an affordable, yet comfortable task chair.



Specifications

W 26-1/2", D 26-1/2", H 32-3/4"-37-3/4" Seat: W 18", D 18", H17-1/4" - 22-1/4" (upholstered add 1") Arms to Floor: 26" - 31" COM ydg seat: 3/4

Stools

W 27-1/4", D 27-1/2", H35-1/2" - 43" Seat: W 18", D 18", H 20" - 27-1/2" (upholstered add 1") COM ydg seat: 3/4

Designed by Giancarlo Piretti.

KI is a registered trademark of Krueger International, Inc.

© 2011 KI All Rights Reserved. Litho in USA. Code KI-00769R2/HC/IP/411

Printed on FSC certified paper using only vegetable-based inks, including metallics. Please recycle.



Mixed Sources Froduct group from well-managed forests, controlled sources and recycled wood or fiber www.fsc.cog Cert no. SW-COC-001885 01395 Forest Stewardship Council





800 Series Stools

From left to right: $818BA - 19^{\circ}-27^{\circ}$ adjustable height stool with cushioned vinyl seat and vinyl back. $824B - 24^{\circ}$ fixed height stool with cushioned vinyl seat and vinyl back. $830A - 31^{\circ}-39^{\circ}$ adjustable height stool with cushioned vinyl seat.



Mechanical Stools

From left to right: ATSSM.1723 – 17"-23" adjustable height stool with hardboard seat. ATPBM.1925 – 19"-25" adjustable height stool with plywood seat and plywood back. ATUBM2632 – 26"-32" adjustable height stool with vinyl seat and vinyl back.

800 Series Stools

Provide an upholstered 1-1/8" thick seat cushion.

- 3 fixed stool heights available 18", 24", 30" with replaceable polyethylene feet
- 3 adjustable heights available 19"-27", 25"-33", and 31"-39" with self-adjusting glides
- Steel or upholstered backrests with adjustable height and depth

Demo is being Scheduled

Mechanical Stools


Combine economy with structural integrity.

- 3 adjustable heights available 17"-23", 19"-25", and 24"-30" with self-adjusting glides
- Steel seat only available without back; plywood or upholstered seats have pivoting backrest with 2" vertical and 2" horizontal adjustment
- Upholstered seat has 2" cushion


Approved by user group 1/25/13

DuraLite® Folding Tables

lightweight | strong | rugged

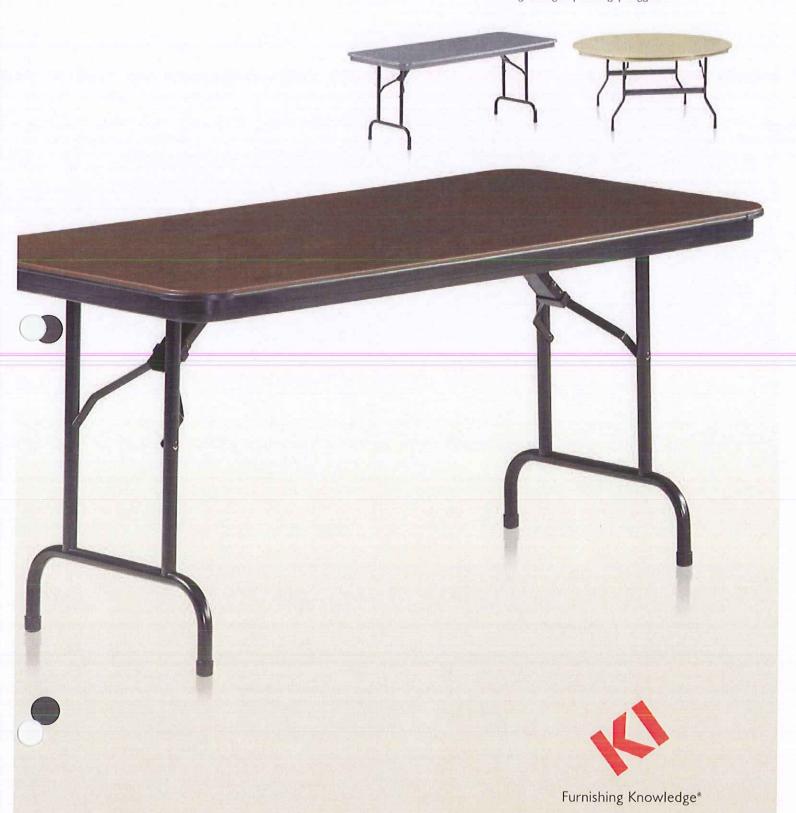

The ultimate lightweight folding table solution.

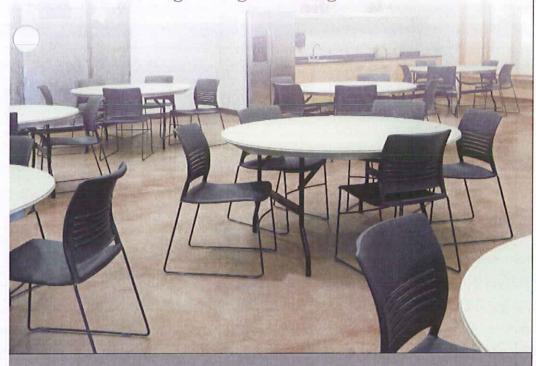


Choose the light one.

Rectangular tables are available in three sizes with sand, blue grey or smooth walnut finishes and black frames (see colors on the right). Round tables are available in two sizes with sand or blue grey finishes and black frames.

Amazingly strong, yet airy hexagonal structure offers unprecedented, weight bearing strength.

DuraLite tables hold a ton of weight: 2000 lbs evenly distributed.



Strong metal-to-metal attachments provide maximum holding power and ensure screw holes won't strip. Legs are easily replaceable.







Printed on FSC® certified paper using only vegetable-based inks, including metallics. Please recycle.



KI is a trusted expert for furniture and wall systems around the globe. USA | CANADA | MEXICO | UK | EUROPE | ASIA | MIDDLE EAST | AUSTRALIA

1330 Bellevue Street • P. O. Box 8100 • Green Bay, WI 54308-8100 • 1-800-424-2432 • www.ki.com

© 2012 KI All Rights Reserved, Litho in USA, Code KI-00673R2/HC/P/1012 KI and Furnishing Knowledge are registered trademarks of Knueger International, Inc.

DuraLite® Folding Tables

DuraLite folding tables withstand the toughest demands of daily use. The unique honeycomb core, aluminum framework, superior materials, and innovative design result in a lightweight table that is strong and durable.



Easy and Safe

Easily carried be one person, DuraLite tables are perfect for any application that requires repeated set up and tear down (banquets, seminars, catered events and multiuse spaces). The lightweight design also diminishes the risk of back injuries from overexertion.

Strong

DuraLite tables exceed stringent tests for leg strength, weight load, and vertical drops onto hard surfaces. Replaceable corner covers and greater weight-bearing strength result from exclusive design innovations.

Finishes







Walnut (Rectangle Only)

Blue Grey



Black




Furnishing Knowledge"



Learn more about



Approval by user group





SFW123GSC - Product Details

The SentrySafe Electronic Fire-Safe is designed to protect documents, digital media and other valuables from fire, water and theft. With 60% bigger bolts than traditional safes and a pry-resistant hinge bar this safe provides additional security against unauthorized access.

Features:

- ETL verified for 1 hour fire protection of CDs and DVDs up to 1700° F
- ETL verified for water-resistance in up to 8" of water for up to 24 hours
- May be bolted to floor (hardware included)
- UL Classified 1-hour proven fire protection with impact


- 4 large 1-inch bolts 60% bigger than traditional safes
- Pry-resistant hinge bar helps provide additional protection from forced entry
- Dual electronic lock with backlit keys increases security
 - Bright, LED interior lighting to make organizing belongings easier
 - A multi-position shelf to enable easy organization
- Key rack, door tray and door pocket for small, easy-to-misplace items
- Bolt-down hardware included as an additional bonus


Electronic - SFW123GSC Dimensions

Exterior: 17.8in H x 16.3in W x 19.3in D
 Interior: 13.8in H x 12.6in W x 11.9 in D

Capacity: 1.23 ft

• Shipping Weight: 90lbs



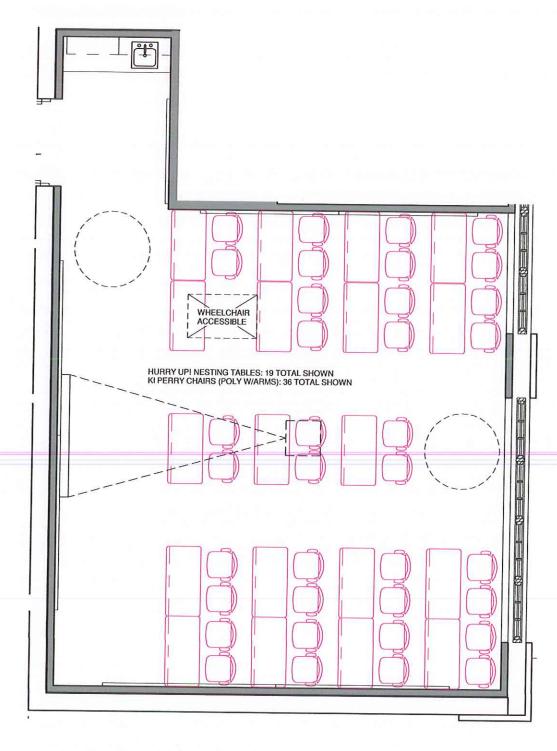


1 CLASSROOM - RM A013 3/16" = 1'-0"

FF&E	DATE:	01/15/13
SAN BERNARDINO VALLEY COLLEGE N T D A R C H I T E C T U R E	JOB NO:	2010-0336-00
9655 Granite Ridge Drive, Suite 400, San Diego, California 92123 San Diego • Los Angeles • Auburn • Visalia • Salinas • Phoenix • Tucson	DRAWING:	FF&E 1

Approved by user group
1/25/13

Hurry Up![®] Tables ■



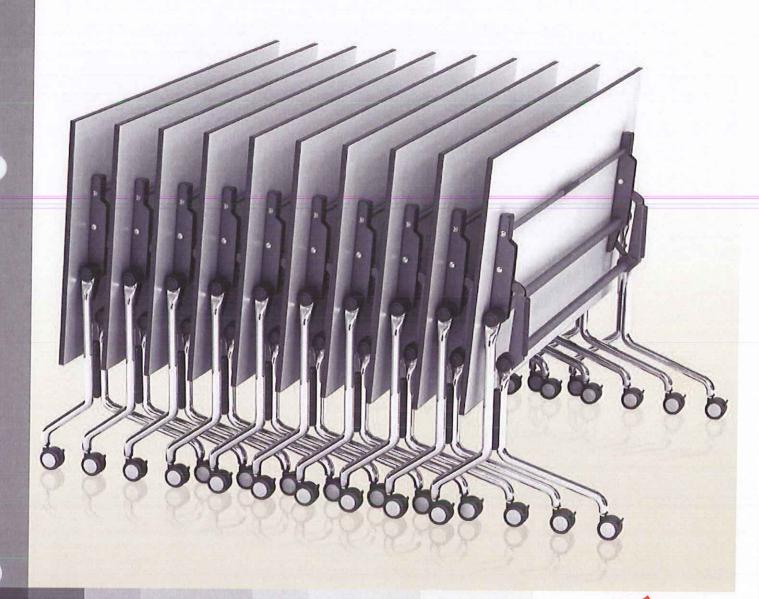

KI Hurry Up! Tables. When you need it yesterday. • Quick to set up

- E
- · Easy to reconfigure
- Simple to store
















The compact nesting ability of the Hurry Up! table is achieved through an innovative leg-within-leg design.




The release mechanism allows one person to flip the table with one motion. Simplicity at work.



Hurry Upl tables are available with an optional lightweight top for even greater ease of movement.









Hurry Up!* Tables

Hurry Up! tables put you on the fast track when it comes to setting up, reconfiguring and storing tables. When you have a table on casters that flips and nests, it just doesn't get much easier.


Flip it.

A quick and simple one-step release enables the top to flip and lock. The leg-within-leg nesting ability of the table and its incredibly narrow folded "envelope" maximize limited storage space.

Nest it.

Pair Hurry Up! tables with Torsion on the Go!*, MI6*, or Strive* Nesting, for the ultimate in mobility, flexibility and compact storage.





Locking gangers add stability to sideby-side configurations.



PowerUp* modules may be embedded for convenient tabletop power supply.



Optional glides offer stability for tables in environments where mobility is less desired.

Edge Options



Laminate; I-1/4" round vinyl bullnose edge; I-1/2" radius corner (54B)



Laminate; I-1/4" flat vinyl T-edge; I-I/2" radius corner (BN)



Laminate; I-1/4" self edge; square corner (64E)



Laminate: 74P edge; square corner (74P)



Laminate; I-1/4" asymmetrical vinyl T-mold impact edge; I-1/2" radius corner (IM)



Laminate; 3/8" x 1-1/4" wood band edge; square corner; corner joint is not mitered (34S)



Laminate; 2-1/4" elliptical molded urethane front edge; 1/4" flat molded urethane on sides/back (ME)

Accessory Options



Under-Table Wire Management

- Easy-to-use, high quality construction
- Harness is fastened to table bottom with screws



Leg Wireways

- · Scuff-resistant, high-impact rigid PVC plastic
- · Two separate wire channels per leg
- · Fastened to legs with adhesive bond
- · One wireway per leg; black only



Grommets

- · Plastic grommets are recessed into table top
- Two grommets per top
- · If grommets are picked, PowerUp[®] cannot be



PowerUp®

- · Includes under-table wire management trough ("KD")
- Includes 2 leg wireways (factory installed)
- Includes 1 to 3 PowerUp[®] modules

Contract Holder

Designed by Giancarlo Piretti.

KI, Hurry Up! and Furnishing Knowledge are registered trademarks of Krueger International, Inc.

© 2011 KI All Rights Reserved. Litho in USA. KI-00496R4/HC/IP/211 Printed on FSC certified paper using only vegetable-based inks, including metallics. Please recycle.



Mixed Sources

Froduct group from well-managed forests, controlled sources and recycled wood or fiber


FSC www.fsc.org Cert no. SW-COC-001886

0 1996 Forest Stewardship Council





Demo is being scheduled



Make your guests comfortable.



An articulate and elegant guest chair.

Renowned sculptor, architect and designer Charles Perry developed the Perry chair and its principle of articulation. The seat is suspended from the lower back, so the occupant's weight perfectly counterbalances the tilting pressure on the backrest.

The seat is suspended from the back so the user's weight perfectly counterbalances the flex of the backrest.

The Perry arm is integral to the frame. A polypropylene armrest is standard.





Gang chairs together with a wire loop ganger.

Dolly holds 25 Perry chairs in polypropylene finish.





Learn more about Perry Stack Chair



GSA Contract Holder

Printed on FSC^u certified paper using only vegetable-based inks, including metallics, Please recycle.



KI is a trusted expert for furniture and wall systems around the globe.
USA | CANADA | MEXICO | UK | EUROPE | ASIA | MIDDLE EAST | AUSTRALIA

1330 Bellevue Street • P. O. Box 8100 • Green Bay, WI 54308-8100 • 1-800-424-2432 • www.ki.com

© 2012 KI All Rights Reserved. Litho in USA. Code KI-00025R4/-C/IP/512 KI and Furnishing Knowledge are registered trademarks of Knueger International, Inc.

Perry® Stack Chair


Wire rod stack chairs are known for low price, small scale and stackability (of course). Stack chairs are not known for comfort.

The Perry stack chair is a surprising exception — a high-density stack chair with a low price, small scale and big comfort. The comfort derives from the chair's back flex, which is counterbalanced by the user's seated body weight. The result is a highly comfortable stack chair.

All three Perry models – armless, with arms and tablet arm – are available in polypropylene, upholstered, or cushioned and upholstered. Select from a wide variety of standard KI upholstery fabrics, Pallas® Textiles or COM.


Designed by Charles Perry.


Specifications:




Armless: W19.5" D21.5" H32.5" Armchair: W23-3/8" D21.5" H32.5" Seat: W18.25" D17.5" H18"





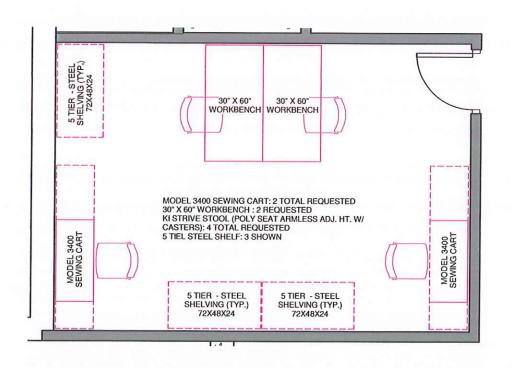


1) COSTUME SHOP - RM A022



2 LAUNDRY - RM A009 1/4" = 1'-0"

FF&E	DATE:	01/15/13
SAN BERNARDINO VALLEY COLLEGE	JOB NO:	2010-0336-00
NTD ARCHITECTURE	DDAMING.	
9655 Granite Ridge Drive, Suite 400, San Diego, California 92123 San Diego • Los Angeles • Auburn • Visalia • Salinas • Phoenix • Tucson	DRAWING:	FF&E 3

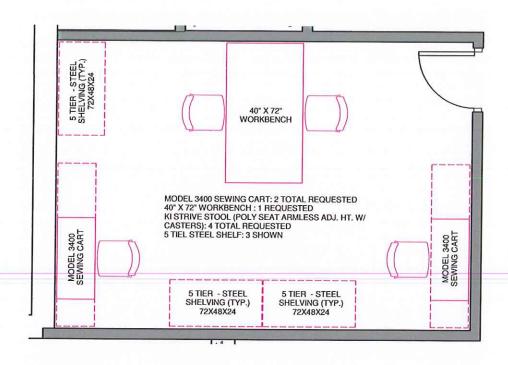

1) COSTUME SHOP - RM A022 - OPTION 2
1/4" = 1'-0"

FF&E	DATE:	02/21/13
SAN BERNARDINO VALLEY COLLEGE	JOB NO:	2010-0336-00
NTD ARCHITECTURE 9655 Granite Ridge Drive, Suite 400, San Diego, California 92123 San Diego • Los Angeles • Auburn • Visalia • Salinas • Phoenix • Tucson	DRAWING	FF&E 3.1





Features

- Insert II System
- Folding Lift
- Contour Laminate Fronts and Leaves
- Notions Tray
- Auto Leaf Support
- Measuring Tape
- Drawer Glide
- U-Casters

Available Options

- #47 Quilt Leaf (42" Wide x 19 3/4" Deep)
- Notions Tray (for inside drawer)
- · Insert Machine Specific
- · Colors: Maple

Companion Units

- #30 Serger Caddy
- #32 Drawer Caddy

Dimensions

- 42" Wide (84" open) x 19 3/4" Deep x 30 1/4" High
- Opening is 24" by 11 5/8"

60 X 30 Maple Square Edge Work Bench- Adjustable Height 1 3/4" Top





Recommend that we use two workbenches, placed together to create a 60"x60" work surface.

Option #1



40" x 72" Cutting Table

Dimensions

Width: 72" (16" closed)

Depth: 40"


Height: 35"

Weight: 127 lbs.

Features

- Melamine (smooth) mar-resistant surface
- Rounded corners for safety
- Large work surface
- Sturdy construction with steel connectors
- Easy roll lockable casters

Approved by Users 1/25/13




Whirlpool Cabrio Platinum 4.6 cu ft High-Efficiency Top-Load Washer (White) ENERGY STAR

Item #: 365109 | Model #: WTW8200YW

Cabrio Platinum 4.6 cu ft High-Efficiency Top-Load Washer (White) ENERGY STAR

- Eco monitor allows you to see the eco-friendliness of each cycle or option you choose and the display rates energy use to show your overall eco-performance
- EcoBoost™ option get additional energy efficiency without giving up cleaning performance; this option lowers a wash
 cycle's overall energy use by reducing water temperature and increasing spin speed
- Unique soft-touch impeller helps move clothes gently through the water allowing the H2Low™ wash system to provide better cleaning performance and gentle fabric care
- H2Low™ wash system includes the unique soft-touch impeller, floating basket technology and circulation spray provides
 optimal cleaning using less water and additives than a traditional top load washer
- Precision dispense senses and adapts to each load, adding detergent, bleach or fabric softener at just the right time; a
 concentrated burst of detergent showers directly onto clothes to penetrate stains and pretreat soils
- · Quiet spin technology offers a unique suspension system that senses each load, making upper-floor installation possible
- Direct drive motor tumbles larger capacity loads, enhances the spin speed for improved energy savings and uses fewer
 moving parts so there's less wear and tear over time
- Quick wash cycle clean small, lightly soiled loads in less time with the fastest wash cycle in its class; plus, increased spin speeds extract more water for faster dry times
- . Designed, engineered, and assembled in the USA

Manufacturer Color/Finish	white	Number of Rinse Cycles	2	Silk Cycle	No	Cycle Status Lights	No
Capacity (Cu. Feet)	4.6	Number of Rinse Temperatures	3	Wool Cycle	No	Estimated Time Remaining Display	Yes
High Efficiency	Yes	Number of Wash Cycles	11	Handwashable Cycle	Yes	Wash Now, Dry Later Option	No
Automatic Load Balancing	Yes	ENERGY STAR Qualified	Yes	Quick/Express Wash Cycle	Yes	End-of- Cycle Signal	Yes
Automatic Temperature Control	Yes	CEE Tier Qualified	CEE Tier III	Bulky/Large Items Cycle			Stainless
Two-Piece Agitator or Impeller	Impeller	Dispensers	Detergent; bleach; fabric softener	Allergen/Sanitary Cycle		Porcelain Lid	No
Matching Pedestal (Model #)	N/A	Control Lockout	No	Programmable Wash Cycles	No	Height (Inches)	45.125
Matching Electric Dryer (Model #)	WED8200YW	Sound Reduction	Yes	Unique/Exclusive Cycle(s)	N/A	Width (Inches)	27.563
Matching Gas Dryer (Model #)	WGD8200YW	Add a Garment	Yes	Whites Cycle	Yes	Depth (Inches)	27.625
Delicate Cycle	Yes	Item Weight (lbs.)	159.8	Soak Cycle	No	Height with Lid Open (Inches)	58

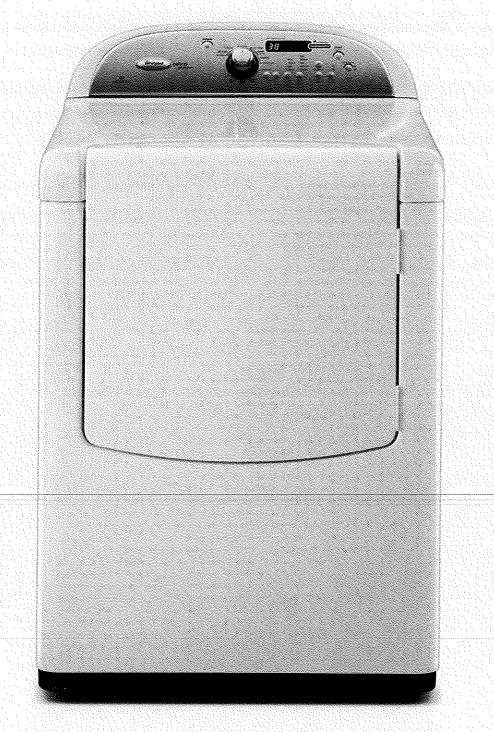

Whirlpool Cabrio 7.4 cu ft Electric Dryer (White)
Item #: 328127 | Model #: WED5600XW

Cabrio Platinum 7.6 cu ft Electric Dryer (White)

- Advanced moisture sensing uses three separate sensors, including moisture strips in the dryer drum, to evenly dry loads without overdrying, reducing the risk of shrinking
- Eco monitor allows you to see the eco-friendliness of each cycle or option you choose; the display rates energy use to show your overall eco-performance
- EcoBoost™ option saves energy by using half of the dryer's dual heating element and extending cycle time; you'll get great drying performance while saving money on utility bills
- Wrinkle Shield™ Plus option tumbles the dryer every 5 minutes for up to 150 minutes after a cycle is complete to help prevent wrinkles from setting into clean, dry fabrics
- Quick dry cycle rapidly dry a small load with the fastest dryer cycle in its class
- High-efficiency dryer uses advanced moisture sensing technology to stop the dryer when clothes are dry and deliver optimal efficiency
- Designed, engineered, and assembled in the USA


Manufacturer Color/Finish	White	Energy Efficient Cycle	Yes	Cycle Status Lights	Yes	Self- Cleaning Lint Filter	No
Dryer Capacity (Cu. Feet)	7.6	Air Dry/Air Fluff Cycle	No	Time Remaining Display	Yes	Window in Door	No
Number of Cycle Selections	9	Delicate Cycle	Yes	End-of- Cycle Signal	Yes	Door Type	Reversible side swing
Number of Temperature Selections	5	Heavy Duty Cycle	Yes	Sound Reduction	Yes	Height (Inches)	45.125
Matching Pedestal (Model #)	None	Permanent Press Cycle	Yes	Eco Monitor	Yes	Width (Inches)	29
Matching Washer (Model #)	WTW8200YW	Timed Dry Cycle	Yes	Drum Material	Painted steel	Depth with Door Closed (Inches)	29.25
Steam Cycles	No	Touch-Up Cycle	Yes	Dryer Rack	No No	Depth with Door Open (Inches)	52.25
Sensor Dry Cycle	Yes	Towels Cycle	No	Control Type	Electronic	Stackable	No
Quick/Express Cycle	Yes	Custom Program Cycle	No	Interior Light	Yes	Item Weight (lbs.)	146
Wrinkle Free Cycle	Yes	NSF Certified Sanitary Dry	No	Check Lint Screen Light	No	Four- Way Venting	No


Approved by users
1/25/13



Z Garment Rack w/Shelf

This easy assembly Z garment rack has a 5-ft base and 5-ft uprights and adds a heavy duty, fold up bottom bottom shelf. The fold up shelf allows you to nest multiple Z racks together when empty. The load capacity is 400 lbs., more than enough to hold your heaviest garments and cartons at the same time. It comes with 4" professional grade, swivel casters with non-marring rubber wheels. The garment rack also includes non-marring, rubber donut bumpers on each corner for added protection, and 2 wheel brakes for extra safety. Also, you may want to consider a rack cover with cover supports to complete your unit. They are listed below as accessories. The assembled size is 63"Lx24"Wx70"H. This unit ships in 2 cartons. **Rack with Shelf available in black or orange.**



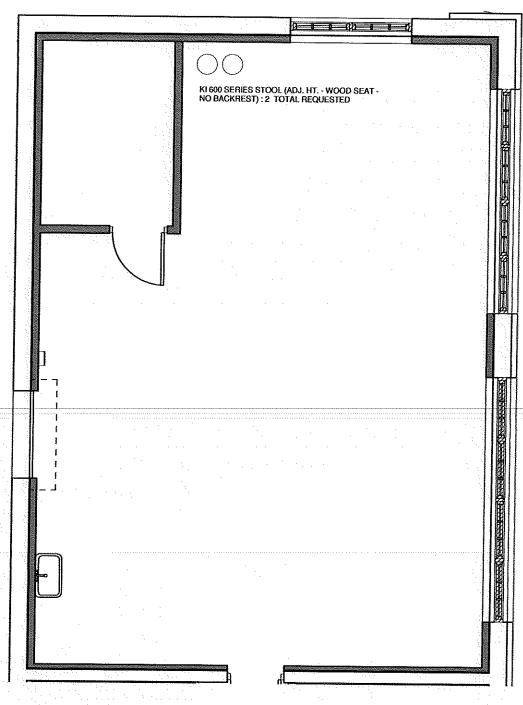

1 WORKSHOP - RM A107 3/16" = 1'-0"

		<u> </u>
FF&E	DATE:	01/16/13
SAN BERNARDINO VALLEY COLLEGE	JOB NO:	2010-0336-00
NTDARCHITECTURE	T	
9655 Granite Ridge Drive, Suite 400, San Diego, California 92123 San Diego • Los Angeles • Auburn • Visalia • Salinas • Phoenix • Tucson	DRAWING:	FF&E 4

Approved by user group 1/25/13

KI all-purpose stools have proven their value in many applications. Moderate pricing and sturdy construction make KI stools an appropriate choice for a wide range of tasks.

600 Series Stools

Get function, versatility and longterm value with a wide selection of styles and options.

- 3 fixed stool heights available 18", 24", 30" with replaceable polyethylene feet
- 3 adjustable heights available 19"-27", 25"-33", and 31"-39"
- Steel or upholstered backrests with adjustable height and depth

Seat Options

- Steel with lacquered hardboard insets
- Upholstered 5/8" foam seat pad in vinyl
- Poly injection-molded polypropylene
- Wood I-I/4" maple seat with clear lacquer finish

Misc. Stools

- Lowboy filing stool 14" high with standard casters or optional polyethylene feet
- 700 Series stool steel seat with hardboard inset and adjustable steel backrest
- Swivel stool 360° swivel with vinyl seat and adjustable vinyl back
- Ivy League stool three heights (18", 24" and 30") with hard (thermoset) plastic seat and swivel glides




600 Series Stools


From left to right: 618P - 18" fixed height stool with poly seat. 624UA - 25"-33" adjustable height stool with vinyl seat. 630BU - 30" fixed height stool with vinyl seat and vinyl back; 624BWA - 25"-33" adjustable height stool with wood seat and steel back.



Misc. Stools

From left to right: 614U - 14" lowboy stool with upholstered seat and casters. 824SB - 24"- 28" adjustable height swivel stool with vinyl seat and vinyl back. 718BA - 18"-26" adjustable height stool with hardboard seat and steel back. ILST.30 -30" fixed height stool with hard (thermoset) plastic seat.



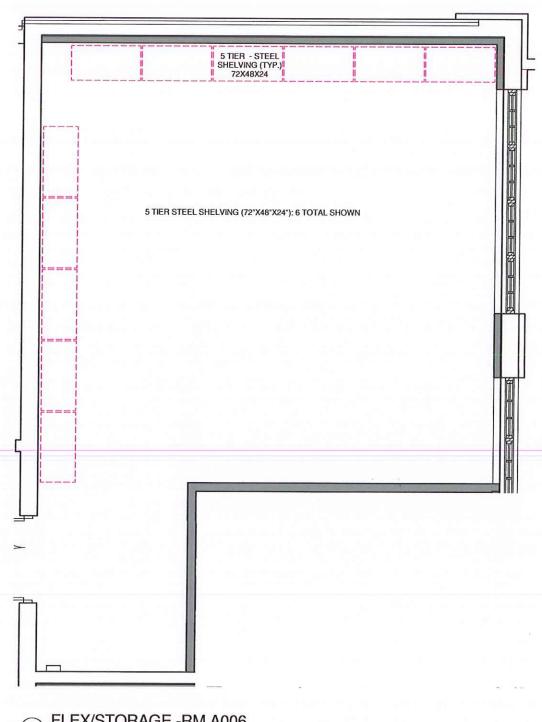

1) FLEX/STORAGE -RM A006 3/16" = 1'-0"

FF&E	DATE:	01/15/13
SAN BERNARDINO VALLEY COLLEGE	JOB NO:	2010-0336-00
NTD ARCHITECTURE	DDAMINO.	
9655 Granite Ridge Drive, Suite 400, San Diego, California 92123 San Diego • Los Angeles • Auburn • Visalia • Salinas • Phoenix • Tucson	DRAWING:	FF&E 2



48"W x 72"H x 24"D

Shelving

(costume shop and flex storage room)

STAGE BOXES



Better than building.

Wenger Stage Boxes will surprise you. In fact, they might just change the way you look at rehearsal furniture. No more painting, repairing or replacing. Made of tough polyethylene, molded one piece construction these stage boxes won't come apart or splinter like wood yet they're lightweight, with built-in handles for gripping. Wenger Stage Boxes are available in multiple sizes that lock together with a revolutionary patented connector that you simply push and thread, no tools required. This makes it easy to create almost any type of rehearsal furniture you need, from stairs to chairs to counters to sofas. Wenger Stage Boxes are sized to the height of standard furniture so that the dimensions of your rehearsal set more closely resemble the performance environment. And when rehearsals are done, Wenger Stage Boxes stack compactly together and store in a small space.

Wenger Stage Boxes - the ideal alternative to building in the scene shop. Besides, your crew has better things to do.







Small Stage Box 16'l x 12' w x 8'h

Wenger
Your Performance Partner

STAGE BOXES





Designed to partner with flipFORM® rehearsal platforms. Configuration above shows four large, 2 medium and 2 small stage boxes with one flipform.

PRODUCT SPECIFICATIONS:

- · Saves time by eliminating construction.
- · Lighter in weight than wood and safer to stack.
- Molded polyethylene construction provides durability and longevity.
- · Black color is through the entire surface so scratches are not as visible.
- Shell has skid resistant texture molded into surface for added safety and sure-footedness.
- Rubber feet prevent box from moving/slipping on smooth surfaces.
- Boxes are sized to mimic basic furniture items and correlate with Wenger staging and flipFORM units.
- Boxes can be combined and connected to create any type of rehearsal furniture.
- No tools are required to connect boxes no clumsy unbolting or unscrewing.
- Patented connection design allows for quick and secure side-to-side, side-to-top, or top-to-top connection.
- · Hollow underside for carrying props and other items.
- · Molded thru-handles for easy transportation by one person.
- Protruding feet nest in recessed pockets to allow boxes to stack securely. One set of three stores in a 24" x 24" x 18" space (61cm x 61cm x 45cm).
- · Five year warranty.
- · Patented.

029A105 Large Stage Box, 32 lb (14.5 kg) 24"w x 24"l x 18"h (61cm x 61cm x 45cm)

029A104 Medium Stage Box, 16 lb (7.25 kg) 12"w x 18"l x 16"h (41cm x 45cm x 31cm)

029A103 Small Stage Box, 8 lb (3.63 kg) 12"w x 16"l x 8"h (41cm x 31cm x 21cm)

USA/8-08/2M/W/LT0137

WENGER CORPORATION
555 Park Drive, PO Box 448
Owatonna, MN 55060-0448
Phone 800.4WENGER (493-6437)
Fax 507.455.4258
Parts & Service 800.887.7145

CANADA Phone 800.268.0148 WENGER CORPORATION
BEIJING REPRESENTATIVE OFFICE
Tel 0086-10-84972502
Fax 0086-10-84972575

WORLDWIDE Phone 1.507.455.4100 Fax 1.507.774.8576

WEB SITE wengercorp.com



Road, Suite 200

SAN JOSE

2033 Gateway Place, Suite 500 San Jose, California 95110 p: 408/573.3635

d Floor 3901 PHOENIX

2800 N. 44th Street, Suite 500 Phoenix, Arizona 85008 p: 602/956.8844 f: 602/956.8866


TUCSON

2940 North Swan Road, Suite 214 Tucson, Arizona 85712 p: 520/784.0975 f: 520/784.0964

VISALIA

4930 W. Kaweah Court, Suite 105 Visalia, California 93277 p: 559/732.1800

t, Suite 100

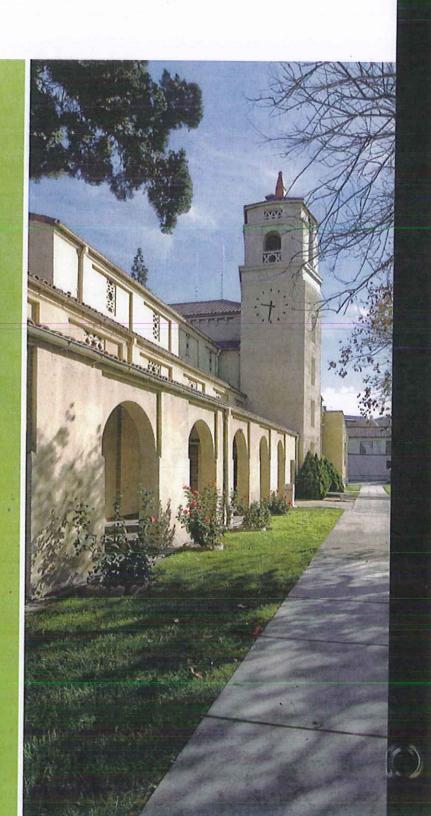

MEETING: SBVC - AUDITORIUM RENOVATION SD USERS GROUP REVIEW

	DESIGN PROPERTY.		
Accommon and the second	NAME	COMPANY.	EMAIL
	RON RETES	KITCHEN/BRJ/SEVILLE	ron. reyes @brjassociates.com
	JASON SMITH	,	ismithoknaconsulting.com
	Larry Kaprielian	LUA	L'Kaprieliano KNA consulting, com
	LENGH ANNE JOE		Ljonese utd.com.
	Brooke Dinear	KBS	Brooke. Duncan & BRIASSENSES
	Laura McLucau	NTO	Luclucase nTd. com
	Fernanua Workine	SBUC	frontinelsbud.cc.ca.us
	Rick Hod lides	5BUC	R.Hrdlicko@SBCO.cc.cA.US
	May Werss	53 C	xwerss@valleycollege.eou
scontonici.	DEG Danip	5 BVC	
Parket Comment of the			
	The second secon		
	The state of the s		
	The second secon		

Campus:		Valley College			
Meeting Date: 1/29	/13	Time:	12:00 PM	End of Meeting:	3:00 PM
Meeting Location:	SBVC	- President Co	onference R	loom	
Employees In Attend	ance				
Employee Name			Emplo	yee Signature	
the Villega:	(10	BS)	2	~	
LEIGH ANNE J	ones	(NTO)	4		
LAURA MCLO	1025		6	2cm	
SCOTT INV	ממא	(KBS)	80	ext / Jum	
Jim Kin	9			em King	
MEMO DA	RAL	A (913VL	1 /	llhy	
JIM KURNOS	545	3BVC		Valle .	20
LAVVYLA	054	1111	1/2/	any nou	eophi
KRIS / ShAF	er	,	1950	SKIL 0	
	avo	(Volum	
Scott Stark			VP	Admin	
Pierce Galyes	-		CAM	pos Police	

KITCHELL/BRJ/SEVILLE
FEB 0 5 2013

Tie.

KITCHELL/BRJ/SEVILLE

Agenda

701 South Mount Vernon, San Bernardino, CA 92399

Phone (909) 693-3160 - FAX (909) 889-9952

DATE

July 17, 2012

FROM:

Michael Villegas, Kitchell/BRJ/Seville

PROJECT

SBCCD - Valley College, Auditorium Renovation Project

MEETING

User Group

TIME

1 30 PM - 3 00 PM

LOCATION

ADSS 207

- 0.0 Project Overview
- 1.0 Project Budget Update
- 2.0 Purpose of Meeting Review DSA Submittal Comments, Bid Add Alternates with User Group, FF&E
 - 2.1 Review DSA Submittal Comments
 - 2.2 Review Bid Alternates presented to President's Cabinet (Option 1 & #2)
 - 2.3 FF&E Overview
- 3.0 New items

KITCHELL/BRJ/SEVILLE

JUL 2 4 2012

\$ P

MEASURE M PROGRAM BUDGET

Program Manager	KITCHELL / BRJ/SEVILLE

Product Matter		1,728 00	213,128 42	213,128 42	0.00		214,856 42		8 13%	Soft Cost Contingency Total
Program Bidget 10,782,985.44 Projected Project			213,128 42	213,128 42	000		214,856 42	-	8 13%	5800 00 Soft Cost Contingency
Program Budget			2,645,630 61	1,909,192 15	736,438 46		2,643,902 61	11 80%	20 74%	Soft Cost - TOTAL
Program Budget										1201 00 Management - 7yrs
Program Budget						ľ		_		2100 00 Classified Management - 7 yrs
Program Budget 10762.085 44 Projected Projecte										2181 OU Classified - / yrs
Program Budget										Bank Processing Fees - /
Infull National Delay 10,725,085 44 Projected Complete 7,393,285 44 Projected Complete 7,393,285 44 Projected Complete 7,393,285 45 Projected Complete 7,393,285 45 Projected Complete 7,393,285 47 Projected Complete Projected Complete 7,393,285 47 Projected Complete Projected Complete Projected Complete 7,393,285 47 Projected Complete Projected Compl										1
Projected Cost Budget										5730 OO Andi Eeee - 7 yrs
Infull National Distriction Program Budget 7,303,285 44 Projected Complete 7,303,285 44 Frogram Budget 7,303,285 44 Frogram Budget 7,303,285 44 Spent to Date 6,84% Frogram Budget 7,303,285 44 Spent to Date 6,84% Projected Complete 7,303,285 47 Spent to Date 6,84% Projected Complete 7,303,285 41 Spent to Date 7,303,285 41 Spent to			70,175 00	70,175 00	000		70.175 00		1 06%	5113 02 Commissioning
Infull National Distriction Program Budget 7,903,265 44 Projected Cost Budget 7,903,265 41 % Spent to Date 684% Projected Cost Budget 7,903,265 41 % Spent to Date 684% Projected Cost Statistics 7,903,265 41 % Spent to Date 684% Projected Cost Statistics 7,903,265 41 % Spent to Date 684% Projected Cost Statistics 7,903,265 41 % Spent to Date 684% Projected Cost Statistics 7,903,265 41 % Spent to Date 684% Projected Cost Statistics 7,903,265 41 % Spent to Date 7,903,265			100,000,00	87,883 79 (12.116.21		100,000 00	0 93%		5113 01 Other Consultants
Infull Nationalion			7,571 43	7,571 43	000		7,571 43	0 07%		6220 786 Program Mgmt - Program Connect
Program Budget			941,395.00	941,395 00	000		941,395 00	8 75%		6220 785 Program Mgmt - Contract
Program Budget			220,952 30	88,000,00	132,952 30		. 220,952 30	2 05%		6220 784 Program Mgmt-Phase 1-& Amendment 1
Projected Comments Project			200	200				 -		6220 79 Legal Consulting
Program Budget 10,762,085 4.4 Projected Cost Budget 7,903,386 4.1 Projected Cost Budget 7,903,386 4.1 Remoration Control to Date Remoration Cost Budget 7,903,386 4.1 Remoration Cost										5620 00 Temporary Facilities - Leasing
Program Budget 10,762,085 44 Frojection Costs tudget 10,762,085 44 Frojection Costs tudget 7,903,385 41 Spent to Date 6,64% Frojection Costs tudget 7,903,385 41 Spent to Date 6,64% Frojection Costs tudget 7,903,385 41 Spent to Date 6,64% Frojection Costs 10,025,646 98 Frojection Costs 10,02										6220 08 Labor Compliance Program
Projected Cost Budget			0.00	0.00	0.00		000		0 00%	6220 38 Insurance - All-Risk
Projected Complete			20,000,00	24,000			20,000,00		0 43%	6220 59 Surveying
Program Budget			00 000 80	34,000,00	1		10,000,00		0,00%	5113 U3 Moving
Projected Control Proj		ŧ	40 000 00	20,000,00	000		40,000,00		7 OF 70	0220 20 IIIspectroli services (ION)
Projection Pro			191 728 00	191 728 00	080		190 000 00		2 87%	SOOD OF Interesting Sections (IOD)
Projected Control Proj			7,000 00	7.000 00	000		7 000 00		0.11%	EDDO 14 Advertising
Program Budget			15,000 00	13,056 61	1,943 39		15,000 00		0 23%	6220 24 Printing
Program Budget			73,600,00	35,800 00	37,800.00		73,600 00		1 11%	6220 22 Plan Check & Agency Fees
Program Budget			40,000 00	27,940 00	12	1	40,000 00		0 60%	6220 13 Testing/Special Testing
Program Budget 10,762,085 44 Projected 736,438 46 Projected 6 84% Soft-Cost Budget 7,903,326 41 % Spent to Date 6 84% Soft-Cost Budget 7,903,326 41 % Spent to Date 6 84% Projected Cost 5 84% Soft-Cost Budget 7,903,326 41 % Spent to Date 6 84% Projected Cost 7,903,326 41 % Spent to Date 6 84% Projected Cost 7,903,328 41 Soft-Cost 7,903,328 41 Soft-Cost 7,903,328 41 Soft-Soft-Soft-Soft-Soft-Soft-Soft-Soft-			909,608 88	373,748 68	535,860.00		909,608 88		13 73%	6220 10 Architectual Fees
Program Budget 10,762,065 44 Projected 736,438 46 Projected] -	2,858,759 03	2,122,320 57	736,438 46	26 56%	2,858,759 03	Prog Value	Construction Value	PROJECT-RELATED SOFT COSTS
Program Budget		(Over)/Under Budget	orecast Total Cost	•					Based On	⊸Obj Code Item
Program Budget 10,762,085 44 Total Spent to Date 736,438 46 Projected Coordinate 736,438 4			k	P	H			000513		
Projected Constitution Projected Constitut	7 1 1 7		ı,				400,000 00			8
Program Budget 10,762,085 44 Total Spent to Date 736,438 46 Projected Cost Budget 2,858,769 03 26 56% Forecast to Complete 10,025,646 99 Projected Cost Budget 2,858,769 03 26 56% Forecast to Complete 10,025,646 99 Projected Cost Budget 2,858,769 03 26 56% Forecast to Complete 10,025,646 99 Projected Cost Budget 10,025,646 99 P			400,000,00	400,000,00	200		400 000 00	147.701	I AGM COLOR	64 IU 47 AV / Technology
Program Budget 10,762,085 44 Total Spent to Date 736,438 46 Projected			100 000 00	100,000,00	000		100,000,00	1 4702	New Collet	6400 /3 Furniture
Program Budget 10,762,085 44 Total Spent to Date 736,438 46 Projected Color			150 000 00	150 000 00	3		150 000 00	2000	Now Const	CASO TA Coming of Equipment
Program Budget 10,762,085 44 Total Spent to Date 736,438 46 Projected Const Budget 7,903,326 41 % Spent to Date 6 84% Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 7,903,326 41 % Spent to Date 6 84% Projected Const Budget 7,903,326 41 % Spent to Date 7,903,326 41 Projected Const Budget 7,903,326 41 Pro			150 000 00	150 000 00	000		150 000 00	2000	Nau Const	GIO 74 February Common
Program Budget	,				. !					OTHER HARD COCTS
Program Budget			683,828 93	683,828 93	000		683.828 93		10 00%	5809 00 Construction Contingency
Program Budget								1		
Total Spent to Date Sp										
Program Budget			į							
Program Budget										
Total Spent to Date						ļ				
Total Spent to Date			6,819,497 48	6,819,497 48	000		6.819.497 48	_		Construction Costs - TOTAL
Total Spent to Date			000	000	000		000			6220 26 CM Fee-Remodel Construction
Program Budget		000	6,626,349 33	6,626,349 33	000		6,626,349 33	61 57%		6220 50 Remodel Construction
Program Budget										6210 26 CM Eas-New Construction
Total Spent to Date										6210 50 New Construction
Total Spent to Date										6120 26 CM Fee - Site Work
Total Spent to Date										6120 50 Site Work (incl Utilities)
## Renovation Program Budget 10,762,085 44 Hard-Cost Budget 7,903,326 41 Soft-Cost Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Cost Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Cost Budget 736,438 46 Projected Cost Budget 7,903,326 41 All Hard Costs - TOTAL 7,903,326 41 Spent to Date Frogram Budgets 7,903,326 41 All Hard Costs - TOTAL 7,903,326 41 Projected Cost Projected Projected Projected Projected Projected Projected Projected Projected Proj		000	193,148 15	193,148 15	000		193,148 15			5420 00 OCIP
Auditorium Renovation Program Budget 10,762,085 44 Hard-Cost Budget 7,903,326 41 Soft-Cost Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Cost Budget 7,903,326 41 Forecast to Complete 10,025,646 98 Projected Cost Projected Cost Budget 7,903,326 41 Forecast to Complete 10,025,646 98 Projected Cost Projected Projected Cost Projected Projected Cost Projected Cost Projected Cost Projected Cost Projected Projected Cost Projected Proj										CONSTRUCTION COSTS
Auditorium Renovation Program Budget 10,762,085 44 Projected Congram Soft-Cost Budget 2,858,759 03 26 56% Soft-Cost Budget 2,858,759 03 26 56% Forecast to Complete 10,025,846 98 Projected Cost Budget 2,858,759 03 26 56% Forecast to Complete 10,025,846 98 Projected Cost Budget 2,858,759 03 26 56% Forecast to Complete 10,025,846 98 Projected Cost Budget 10,025,846 98 Pro		0 00	7,903,326 41	7,903,326 41	000		7,903,326 41	Costs - TOTAL	All Hard	
Auditorium Renovation Program Budget 10,762,085 44 Total Spent to Date 736,438 46 Projected Const Budget 7,903,326 41 % Spent to Date 684% Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Const Budget 2,858,759 03 26 56% Forecast to Complete 10,025,646 98 Projected Projecte	Comments	(Over)/Under Budget	orecast Total Cost	onecast to Complete F	Date	Comments	Onginal Budgets		GOSII;S S	
Auditorium Renovation 42-37-37-39 (7-00-0-22-2) - 100	The state of the s	HEREK K BERRAL		THE WATER OF THE PARTY OF THE P						
Auditorium Renovation Program Budget 10,762,085 44 Total Spent to Date 6 84% Hard-Cost Budget 7,903,326 41 **Spent to Date 6 84% **Projected Program Costs 7,903,326 41 **Spent to Date 6 84% **Projected Construction Costs 7,903,326 41	(Over Budget)	•	2,858,759 03	ected Soft Costs	Pro.	10,025,646 98	Forecast to Complete	26 56%	2,858,759 03	Soft-Cost Budget
Auditorium Renovation 42-31-331-3017-3000-32201 100		000	7,903,326 41	Instruction Costs	Projected Co	684%	% Spent to Date		7,903,326 41	Hard-Cost Budget
Auditorium Renovation 42-31-331-4-000-52201 IOU	(Over Budget)	000	10,762,085 44	d Program Costs	Projecte	736,438 46	Total Spent to Date		10,762,085 44	Program Budget
					_		11-0000-02401 100	1 50 75 75 T		TROUBLE ROUTING AND

120

MEASURE M PROGRAM BUDGET

BERVICES SERVICES ERVICES (#1) (#1-Suppon) (#1-Suppon) (#1-Relmb) (anaggemen) (anaggemen) (anaggemen) TES	UDGETS BY Contract or PO # 123173 121068 121073 122170 123466 123263 110936 120653 123653 123653		All CO's / Augment 12,060 00 3,120 00 3,675 00 3,040 00 0 00	Current Confried Value 50,200 00 10,000 00 12,960 00 37,890 00 37,890 00 37,900 00 191,728 00 191,728 00 14,044 16 16,380 94 941,395 00 795,075 00 3,000 00 3,000 00 3,000 00 3,000 00 3,000 00 3,000 00 3,000 00		Forecast to Complete 1 50,200 00 8,056 61 70 00 22,895 54 170 00 -17,28 00 00 -17,28 00 00 00 00 00 00 00 00 00 00 00 00 00	COSTS BY VENDOR COSTS BY VENDOR FORESAST Total Contract Forecast Total 50,200 00 0 00% 11 10,000 00 0 00% 12,060 00 10,00% 170 00 0 00% 170 00 0 00% 170 00 0 00% 170 00 0 00% 170 00 0 00% 170 00 0 00% 1728 00 0 0 00% 1728 00 0 00% 1728 00 0 00% 1728 00 0 00% 1727 20 0 0 00% 1727 20 0 0 00% 1727 20 0 00% 173 20 00% 174 3 00% 175 11 43 0 00% 175 11 43
6220 59 INIPES-DYE ASSOCIATES 6220 59 INTATE OF CALIFORNIA PLACE HOLDERS 6220 10 Archaerus Fees	120653 123262	3,600 00	3,040 00 0 00	3,040 00 3,600 00 114,533 88	3,600 00 0 00	2,933 44 0 00 114,533 88	3,040 3,600 114,533
6220 10 Architectual Fees 6220 13 Testing/Special Testing 6220 22 Plan Check & Agency Fees		27,940 00 35,630 00		114,533 88 27,940 00 35,630 00	0000		27,940 35,630
6220 24 Penting - 6220 14 Adventising - 5113 03 Moving - 6220 59 Surveying - 6220 59 S	,		1 1 1	7,000 00 40,000 00 21,960 00	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	7,000 00 40,000 00 21,960 00	7,000 40,000 21,960
6220 782 KITCHELL (Amendment #1) 5113 01 Other Consultants 5113 02 Commissioning		28,000 00 64,990 00 19,975 00		28,000 00 64,990 00 19,975 00	3000	28,000 00 64,990 00 19,975 00	28,000 00 64,990 00 19,975 00
6410 74 Extures & Equipment 6410 73 Furniture		150,000 00		150,000 00	0000	150,000 00	150,000 0
6410 47 AV / Technology 5420 00 COIP 5800 00 Soft Cost Contingency 5800 00 Injend Inspection Services	>	193,148 15 214,856 42 -1,728 00	:	193,148,15 214,856,42 -1,728,00	00000	193,148,15 214,856,42 -1,728,00	193,148 15 214,856 42 -1,728 00
5809 00 Construction Contingency		683,828 93		683,828,93	0.00	683,828 93	683,828 93
							:

HTD
ARCHITECTURE

SBVC AUDITORIUM RENOVATION

COST ANALYSIS

	BASE COST	VALUE ENGINEERING		OPTION # 1		OPTION (I			
OTAL BLDG COST	\$ 4,988,150.00		\$ 4,988,150.00			OPTION #2		(0) dpt(on #3)	
- A		Re-use Electrical panels			\$ 4,988,150.00	//////////////////////////////////////	\$ 4,988,150.00		1
		No duo Electrical pariera	\$ (22,000.00)	Re-use Electrical panels		Re-use Electrical panels	\$ (22,000.00		\$ 4,988,1
				Hydraulic Elevator	\$ (30,000.00)	Hydraulic Elevator	\$ (30,000.00	its aso Electrical balls	
TE	\$ 1,003,000,00	Commission of the Commission o				πορλ ³ ' ''''''	(00,000.00	Hydraulic Elevato	or \$ (30,00
	***************************************		\$ 1,003,000.00		\$ 1,003,000.00		\$ 1,003,000.00		
				Site Demolition		Site Demolition			\$ 1,003,00
				East Side Improvements		East Side Improvements		Z Site Demonstration	
				West Side Improvements		West Side Improvements		Last one improvement	
			Ì	South Side Improvements	\$ (134,000,00)	South Side Improvements	\$ (49,000.00	vica: Olde implovement	s \$ (49,00
				Site Lighting		(2)	\$ (134,000.00	ZL Occur olde intolovernens	s \$ (134,00
udio Visual rough -In	400,000,00				<u> </u>	Site Lighting	\$ (215,000.00	Site Lighting	9 \$ (215,00
idio visuai rougn -in	\$ 100,000.00	- The same of the	\$ 100,000.00		\$ 100,000,00				
					100,000.00		\$ 100,000.00		\$ 100,00
eatrical Equipment (fixed)	\$ 325,850.00		\$ 325,850.00		\$ 325,800,00				
	i i	Reduce number of motorized line sets	\$ (18,000.00)	Deduct Studio Theatre lighting console	\$ (5,000.00)	7	\$ 325,800.00		\$ 325,80
				Eliminate motorization of main drape	\$ (31,000.00)	Deduct Studio Theatre lighting console		Deduct Studio Theatre lighting console	\$ (5,00
				Reduce number of motorized line sets	\$ (18,000.00)	Eliminate motorization of main drape	\$ (31,000.00)	Eliminate motorization of main drape	\$ (31,00
				Change variable speed motorized hoists to fixed	3 (18,000.00)	Reduce number of motorized line sets	\$ (18,000.00)	Reduce number of motorized line sets	\$ (18.00
				speed	\$ (19,000,00)	Change variable speed motorized hoists to fixed		Change variable speed motorized hoists to fixed	1 (10,00
				d pecca	(19,000.00)	speed	\$ (19,000.00)	\$peed	
OTAL (w/o EQUIP)	\$ 6,417,000.00		\$ 6,377,000.00		£ 5 700 050 00				(10,000
	***************************************		+ 0,011,000,00		\$ 5,768,950.00		\$ 5,768,950.00		\$ 5,768,950
idio Visual (loose equip)	\$ 496,000,00	Audio Visual (no fixed)	e 407,000,00	Audio Visual:					\$ 5,700,950.
1	,	Auditorium - Audio: \$298,000	\$ 497,000.00		\$ 310,000.00	Audiovisual:	\$ 252,000,00	Audiovisual:	
		Auditorium - Video: \$94,000		Auditorium - Audio: \$206,000		Auditorium - Audio: \$220,000	+ 202,000.00		\$ 293,000
		Black Box Audio: \$73,000		Auditorium - Video: \$0		Auditorium - Video: \$0		Auditorium - Audio: \$220,000	1
		Classroom/ Greenroom & Audio Video: \$32,000		Black Box Audio: \$73,000		Black Box Audio: \$0		Auditorium - Video: \$0	1
		Classiconia Greentootti & Audio Video: \$32,000		Classroom/ Greenroom & Audio Video: \$32,000		Classroom/ Greenroom & Audio Video: \$32,000		Black Box Audio: \$73,000	
reatrical ((loose equip)	\$ 101.750.00	Theatrical (no fixed)				7,000 Fig. (02,000		Classroom/ Greenroom & Audio Video: \$0	1
teatreus (tioose equip)	9 151,750.00	Theatrical (no fixed)	\$ 191,750.00	Theatrical:	\$ 191,750.00	Theatrical:	6 404.750.00		
				Eliminate Auditorium lighting truss and motors	\$ (10,000.00)		⇒ 191,/50.00	Theatrical:	\$ 191,75
				Reduce quantity of automated lights in stage lighting		Reduce quantity of automated lights in stage lighting			
	1			equipment from (5) to (2)	\$ (22,500.00)	equipment from (5) to (2)		Reduce quantity of automated lights in stage lighting	
	i i			Eliminate Studio Theatre platform and seats (shop	(,-,-,0,0)	equipment (5) to (2)	\$ (22,500.00)	equipment from (5) to (2)	\$ (22,500
OTA!	0740477000			built)	\$ (46,250.00)			Eliminate Studio Theatre platform and seats (shop	, , , , , , , , , , , , , , , , , , , ,
OTAL	\$ 7,104,750.00		\$ 7,065,750.00		\$ 6,191,950.00		\$ 6,190,200.00	built)	\$ (46,250

